

CONSTRUCTION UPDATE

Work Accomplished

The project construction is progressing very well with the majority of the storm sewer and private utility relocation work completed. This has allowed the contractor to proceed with construction of the new pavement and retaining wall structures.

ROADWAY

The majority of the mainline paving along O Street between 48th Street and 52nd Street was completed and the contractor is currently working on mainline paving on O Street between 45th Street and 48th Street.

It is anticipated that the majority of the paving on O Street between 45th Street and 48th Street will be completed by June 16th.

WATER MAIN

The water main construction between 37th Street and 48th Street is nearly complete and the new main has been placed in service between 40th Street and 48th Street. The contractor is currently connecting the water services for the adjacent properties up to the new main between 37th Street and 38th Street.

It should be noted that the contractor was able to complete the water main work in this area without having to close 40th Street at O Street as originally anticipated.

It is anticipated that the water main work between 33rd Street and 44th Street will be completed by June 30th.



O Street at 52nd Street, looking west, June 5, 2006



O Street at 52nd Street, looking west, May 23, 2006

Upcoming Work/Changes in Traffic


ROADWAY

The contractor has started driveway reconstruction work along O Street between 48th and 52nd Streets and will continue with this work along O Street as retaining wall and pavement construction is completed. The contractor is scheduled to begin pavement construction along the east side of 48th Street the week of June 12th.

WATER MAIN

The contractor will shift eastbound traffic back to the south side of O Street

continued on back

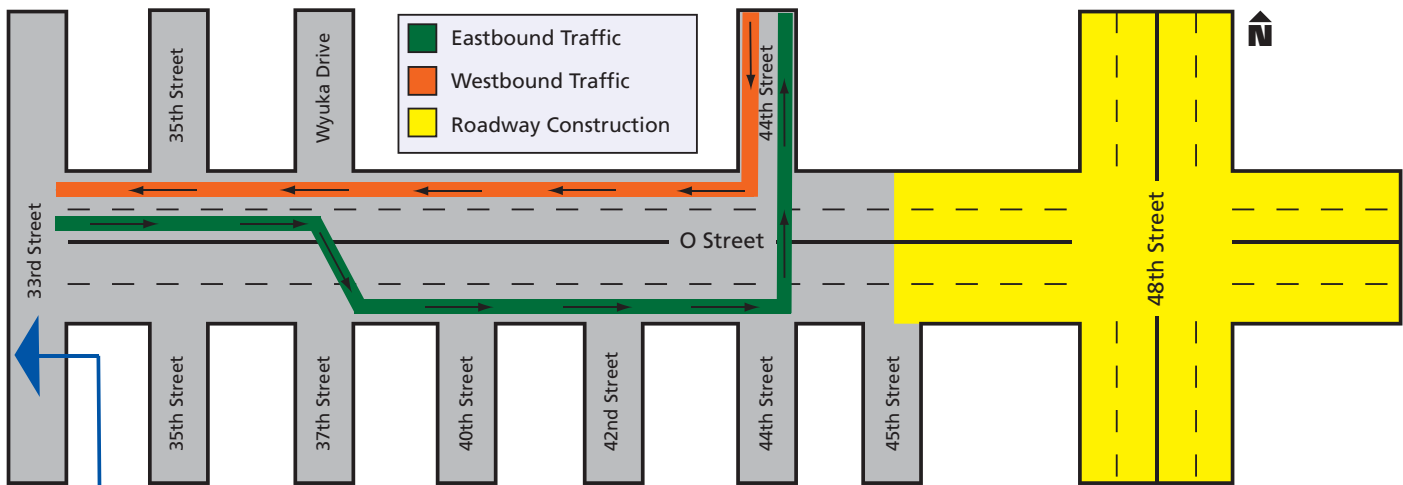

Left turns will be restricted starting June 8th or 9th and last approximately 14 days

A traffic shift is scheduled for June 12th.

between 37th Street and 44th Street in the near future to allow the Contractor to reconstruct the raised medians along this segment of the roadway. **The traffic shift is scheduled for June 12th.** Once eastbound traffic is shifted back to the south side of the roadway, drive access to businesses along the south side of O Street will be limited to right in and right out movements similar to the pre-construction conditions.

The Contractor will begin water main work at the southeast corner of the 33rd and O Street intersection on June 9th. Northbound through traffic on 33rd Street will be maintained during this time, however the northbound to westbound left turn movement will be restricted. This work is anticipated to take approximately 14 days. Drivers who utilize the northbound to westbound left turn movement should seek alternate routes during this time period.

Following completion of the water main work at the southeast corner of 33rd and O Street, the existing water main will be abandoned at 33rd Street. This will require a shift to the south side for both eastbound and westbound traffic on O Street between 32nd Street and 35th Street along with total closure on 33rd Street between O Street and P Street. Once the water main abandonment work at 33rd Street is completed, traffic on O Street will be shifted to the outside lanes to allow the median

reconstruction to be completed between 32nd Street and 37th Street. **Completion of the water main work is anticipated by June 30th.**

For More Information

Visit the project web site at www.ostreetlincoln.com for construction updates, schedule information, maps, photos, driving directions to businesses, and much more.

Or, contact:

Lisa Behrns, Public Participation
 48 and O Street Project Team
 402-458-5992 or ostreet@oaconsulting.com
